ProjectManagement.mpp

ID		ID	Task Mode	Task Name	Duration	Actual Duration	Start	Finish
1		**1**		**Software Development**	**78 days**	**27.06 days**	**Sat 1/14/17**	**Sun 4/30/17**
2	✓	**2**		**Scope**	**6.06 days**	**6.06 days**	**Sat 1/14/17**	**Sat 1/21/17**
3	✓	3		Define Primary Resources	0.5 hrs	0.5 hrs	Sat 1/21/17	Sat 1/21/17
4	✓	4		Create github	0.5 days	0.5 days	Sat 1/14/17	Sat 1/14/17
5	✓	**5**		**Research Project**	**56 hrs**	**56 hrs**	**Sat 1/21/17**	**Sun 1/29/17**
6	✓	**6**		**Team meeting - write ideas from reading project intent statement**	**7 days**	**7 days**	**Sat 1/21/17**	**Sun 1/29/17**
7	✓	7		1	3 hrs	3 hrs	Sat 1/21/17	Sat 1/21/17
8	✓	8		2	3 hrs	3 hrs	Sat 1/21/17	Sat 1/21/17
9	✓	9		3	3 hrs	3 hrs	Sat 1/21/17	Sat 1/21/17
10	✓	10		4	3 hrs	3 hrs	Sat 1/21/17	Sat 1/21/17
11	✓	11		5	3 hrs	3 hrs	Sat 1/21/17	Sat 1/21/17
12	✓	12		6	3 hrs	3 hrs	Sat 1/21/17	Sat 1/21/17
13		**13**		**Analysis / Design Phase**	**7 days**	**0.49 days**	**Fri 1/27/17**	**Mon 2/6/17**
14		**14**		**Function model**	**1 day**	**0.16 days**	**Sat 1/28/17**	**Sat 1/28/17**
15	✓	15		Team meeting - create Use Case Diagram	3 hrs	3 hrs	Sat 1/28/17	Sat 1/28/17
16		**16**		**create Activity Diagram**	**0 days**	**0 days**	**Sat 2/4/17**	**Sat 2/4/17**
17		17		Course Creation and Management	4 hrs	0 hrs	Sat 2/4/17	Sat 2/4/17
18		18		Student Information Management	4 hrs	0 hrs	Sat 2/4/17	Sat 2/4/17
19		19		Student Attendance Management	4 hrs	0 hrs	Sat 2/4/17	Sat 2/4/17
20		20		Grade Management	4 hrs	0 hrs	Sat 2/4/17	Sat 2/4/17
21		**21**		**Structure model**	**1 day**	**0 days**	**Sun 2/5/17**	**Sun 2/5/17**
22		22		class Diagram		0 days		



ID		ID	Task Mode	Task Name	Duration	Actual Duration	Start	Finish
23		23		ER Diagram		0 days		
24		**24**		**Behavior model**	**1 day**	**0 days**	**Fri 1/27/17**	**Fri 1/27/17**
25		25		Sequence Diagram		0 days		
26		26		Verifying and Validating Analysis Models	8 hrs	0 hrs	Mon 2/6/17	Mon 2/6/17
27		27		Development	24 days	0 days	Tue 1/31/17	Fri 3/3/17
28		**28**		**Testing**	**1 day**	**0 days**	**Tue 3/7/17**	**Tue 3/7/17**
29		29		Develop unit test plans using product specifications		0 days		
30		30		Documentation	7 days	0 days	Tue 1/31/17	Wed 2/8/17
31		31		Post Implementation Review	1 day	0 days	Wed 3/8/17	Wed 3/8/17



Resource Names	Predecess
Funing Teng	
Funing Teng	
	2
Funing Teng	
Bhakti Chheda	
Guldasta Kozho	
Hangyi Zhao	
Hardik Parikh	
Tailong Si	
	5
Bhakti Chheda,Funing Teng,Guldasta Kozho,Hangyi Zhao,	
Bhakti Chheda	
Guldasta Kozho	
Hangyi Zhao	
Tailong Si	

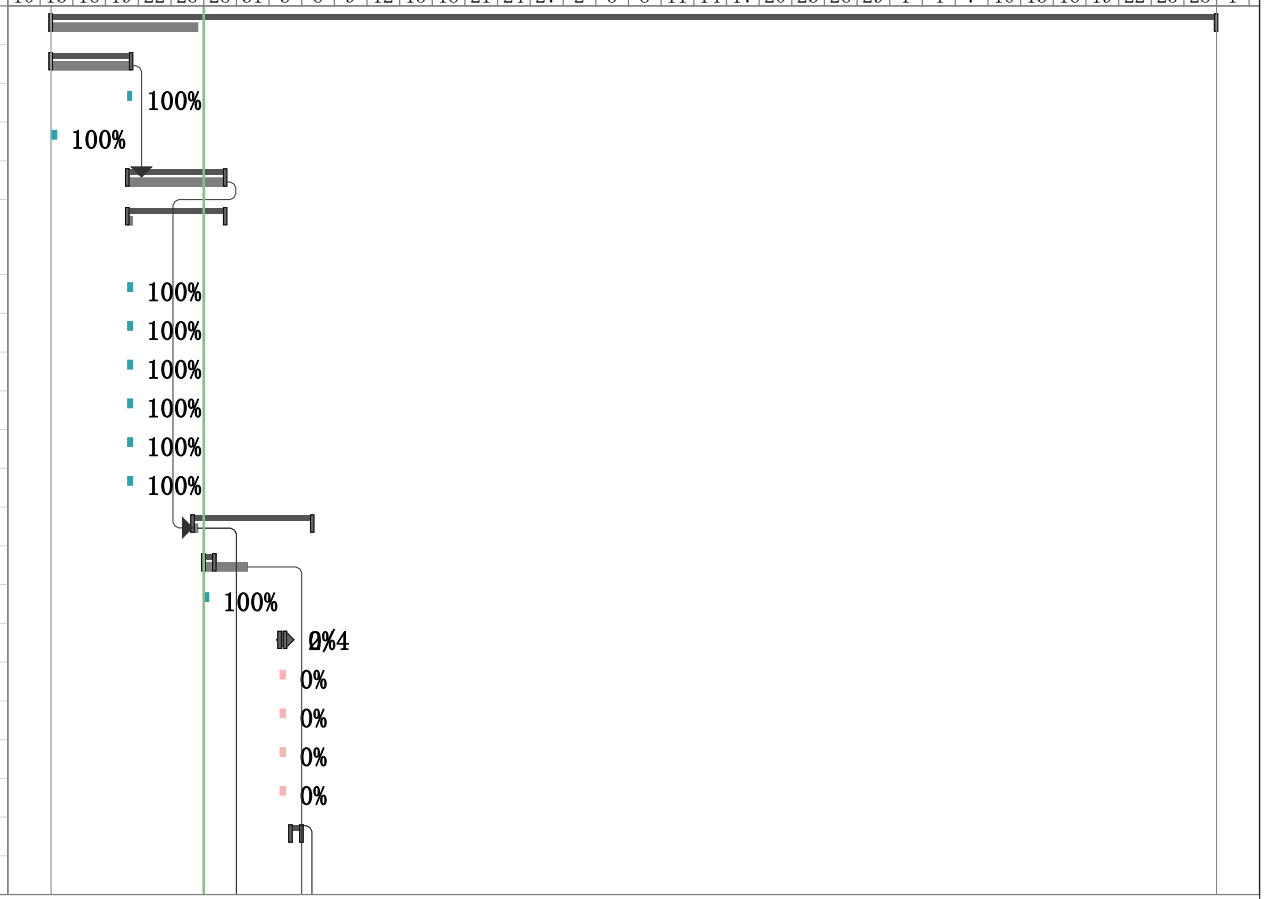

Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	

Resource Names	Predecess
	14,21,24
Funing Teng,Hardik Parikh	13
Guldasta Kozho,Hangyi Zhao,Tailong Si,Bhakti Chheda	**27**
Bhakti Chheda,Guldasta Kozho,Hangyi Zhao,Tailong Si	13
	28,30

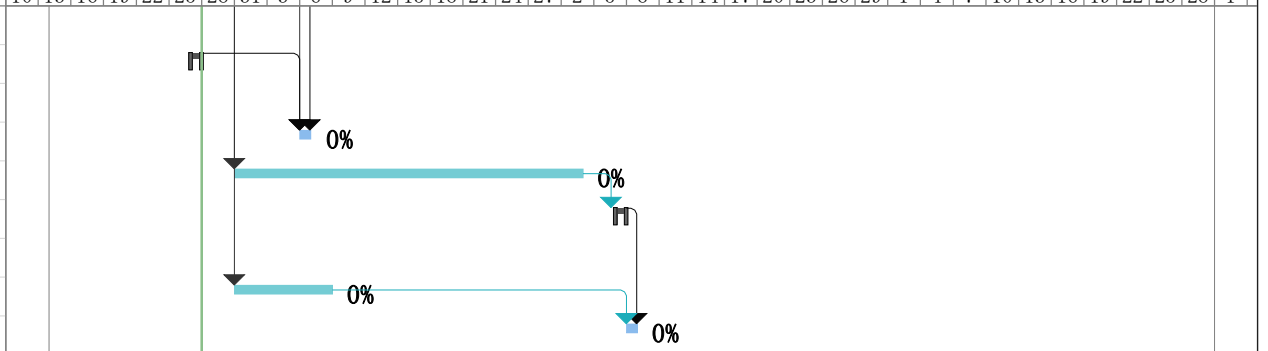

Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	
